

5 Year Environmental Implementation Plan

2019 – 2023
Version 15.0
30 September 2022

Author:	Principal Advisor	Jonathon Dalton
Reviewer:	Manager - Tailings & Environment	Trent Scherer
Approver:	General Manager	Pine Pienaar

Environment Improvement Projects

The environmental improvement project outlined in this implementation plan have been grouped into key focus areas shown in Table 1.

Table 1: Summary of improvement projects

Focus Area	Key Objective
Organisation cultural change	Risk reduction through empowering the entire workforce
Air Quality Management	Emission/particulate and risk reduction
Water Management	Impact mitigation
Land Management	Mitigate contamination: safe, stable and sustainable
Other	Amenity impact reduction

Explanation of the Implementation Schedule

The implementation schedule shown after each project table shows the study, engineering or execution phase, which are described below:

Study Phase

Projects shown in study phase are at the earliest part of the implementation process and require work to identify and assess options that will deliver the required environmental outcome. The outcome of the study phase is to determine the option that best meets the defined performance criteria. In selecting the preferred option during the study phase to take to the engineering phase, options are assessed against a number of criteria, including,

- How effectively each option mitigates the risk,
- Can the project be delivered in the required timeframe?
- What is the cost of each option compared to the expected environmental outcome?
- Can the option be practically constructed?
- Can the option be implemented within an operating refinery?
- What approvals will be required to deliver the option?
- Can the option be delivered safely?

Some projects are quite complex requiring more time and resources in determining the right option. Consequently the outcome of the study phase for a project will deliver the option to take forward to the engineering phase.

Engineering Phase

The engineering phase is where the detailed work is carried out and a set of documents is developed to allow the project to move into the final execution phase. The engineering phase covers traditional mechanical, civil, structural, process and electrical engineering input, which will provide a detailed design that can be constructed to meet applicable Australian, Queensland and QAL standards. Other aspects covered in the engineering phase include any required Commonwealth, Queensland and Local government approvals pertaining to environmental, planning and cultural heritage legislation. These approvals can only commence once the project design is nearing completion.

The output from the engineering phase will be a detailed design and issued for construction drawings (where required) that are based on risk reviews (process, safety, health, environmental and cultural), constructability reviews as well as hazard and operability assessments.

As stated, some projects will require a number of approvals from the Commonwealth, State and Local governments with approval time frames that may extend up to a year during the engineering phase for some of the more complex projects.

Towards the completion of the engineering phase QAL will be able to determine a more detailed performance indicator to demonstrate the environmental improvement at the completion of execution.

Execution Phase

The output of the engineering phase will be a package of work that will generally include a number of deliverables that will be tracked during the execution phase. The type and complexity of the project will determine the number of deliverables required and how the deliverables are phased, as some may need to be finished before another can begin.

How to Interpret the Tables

The study (gold) and engineering (blue) phase schedules are based on delivering milestones at the end of a specified quarter, i.e 2019 Q1 means Quarter 1 2019 January to March. The execution phase (green) schedules are based on delivering milestones within a calendar month.

This example shows the study phase milestone for a project is due in quarter 4 in 2018. This means that during quarter 4 the project will transition into the engineering phase and the implementation plan will be updated accordingly.

Task	Project Name					
	2018		2019			
	Q3	Q4	Q1	Q2	Q3	Q4
Description						

This example shows the engineering phase milestone due in 2019 quarter 2 and the implementation plan will be updated in quarter 2 to show the execution phase.

Task	Project Name					
	2018		2019			
	Q3	Q4	Q1	Q2	Q3	Q4
Description						

This example shows the execution phase will take 1 and a half years with the completion date of the project in April 2020.

Task	Project Name											
	2019				2020				2021			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Project Description												

Organisational Cultural Change

QAL recognises that the culture of an organisation is a significant factor impacting the environmental performance of a business. While leadership commitment and governance structures are important to ensure that environmental improvement projects are effectively executed; our environmental improvement program will only succeed if we empower all of our employees to have due and proper consideration of environmental obligations and risks in their everyday tasks.

Redefining our site culture begins with our workforce having a greater understanding of the process safety aspects of our operation, and the significant potential environmental and community impact our operations can have. We then need to empower our workforce to reduce risk around process and environmental concerns to avoid them and respond when potential process safety and environmental concerns arise. The introduction of a disciplined system for organizing workplaces and the broader QAL operating environment is underway.

Improved housekeeping and understanding of process safety critical controls will lead to early detection of leaks, spillage and situations that could lead to potential environmental impacts.

Project (C1)	Site Cultural Change
Risk class	- IV/Critical
Environmental risks	- Failure of systems causing environmental incidents that impact on the receiving environment and community
Project solution / options	<ul style="list-style-type: none"> - Improve process safety and environmental risk detection for all QAL employees through a Process Safety Management System (PSMS) that ensures critical controls are identified and verified. - All QAL employees involved with ensuring critical controls are in place are aware of the importance of these controls and that they will be verified. - Cultural change will be incorporated into the operations systems including: <ul style="list-style-type: none"> • Functional workplace program • Annual environmental training for all employees • Daily HSE meetings (environment in work preparation) • Quarterly business updates, led by site senior executives • Routine engagement surveys • Purple banner reporting which includes the introduction of reporting category focused exclusively on environmental incidents
Objective / performance outcome	<ul style="list-style-type: none"> - Greater awareness of environmental risk and employee's role in controlling these risks. - Improved culture relating to process safety and environmental risk management throughout the entire organisation through the implementation of a PSMS.
Performance Indicator	<ul style="list-style-type: none"> - 90% of major hazard critical control health checks completed within the first 12 months after the PSMS is implemented across site (end of 2020). - Greater than 95% of employees completing annual environmental awareness training.
Cost estimate A\$ million	- \$1 annually
Project Stage	<p>Executed</p> <ul style="list-style-type: none"> - PSM Major Hazards defined, reviewed and results of the activities that determine if critical controls will work when called upon reviewed monthly by the Management Team.

Comments	<ul style="list-style-type: none"> - At least one example of functional workplace implemented in every section onsite, with several in many sections. Continued deployment required until full site coverage is achieved. Dedicated team now supporting the functional workplace implementation to ensure progress is maintained. - All PSM major hazard workshops complete with monthly results reported to the board. <ul style="list-style-type: none"> • CCMP process (deep dive by GM on Critical Controls) ongoing on completed major hazards. • Monthly managers review process implemented and chaired by General Manager. • A Pathway-to-Compliance has been developed for every Major Hazard and is tracked monthly. • Two independent consultants are currently reviewing the PSM system to look for opportunities to make it even more robust. - Annual environmental training updated and implemented in January; <ul style="list-style-type: none"> • >95% of employees have completed Environmental Web Based Training in 2022 (>95% in 2018-21). - ERM organisation psychologist team supporting the organisational cultural change process, including: <ul style="list-style-type: none"> • Development of >75 actions focusing on environmental stewardship, • Actions are fully integrated into the QAL Business Strategy, <ul style="list-style-type: none"> ▪ Functional workplace, waste minimization, including significantly increasing recycling, and actions arising out of the QAL Environment Committee remain the primary focus areas in 2022. •
----------	---

Implementation Schedule

Site Culture Change										
Task	2018		2019				2020			
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
Site Cultural Change	Complete		Complete				Complete			
	Study	Engineering		Execution						

Air Quality Improvement Projects

QAL's 5-year air quality improvement plan, supported by targets, actions and programme of works is summarised below. Capital spend is estimated at between A\$19 million to A\$38 million.

Project (A1)	Alkali Release Off-Site
Risk class	- IV/Critical
Environmental risks	- Alkali release to atmosphere with potential to impact air quality and property in the surrounding communities
Project solution / options	Identify sources at the refinery that can release alkali and put in place measures to reduce the risk of the release occurring.
Objective / performance outcome	<ul style="list-style-type: none"> - Sources will be identified where actions can be taken to reduce likelihood and consequence of alkali release - Reduce identified Class III and IV alkali release risks to Class I and II to mitigate impact to the community
Performance Indicator	<ul style="list-style-type: none"> - No alkali release events from completed projects due to QAL operations or maintenance activities - All emission sources assessed IV risk are identified and an engineering solution is developed or investigations exhausted to reduce risk to Class I and II.
Cost estimate A\$ million	- 26.0

<p>Project Stage</p>	<p>Execution</p> <ul style="list-style-type: none"> - Digestion relief system - containment system <ul style="list-style-type: none"> • The design will look at improving separation of steam and slurry through: • More efficient design of the entrainment separators, • Improving separation efficiency in the relief tanks. It is expected that the Unit 2 relief tank will be replaced as part of this project. Improvements in Unit 1 and 3 relief tanks have already been delivered through removal of redundant equipment inside the relief tanks. • Long lead procurement for the valves has been approved. - Digestion relief system – front end. <ul style="list-style-type: none"> • Installation of slurry shut off valves between the digester and the first flash tank to stop the flow of energy from the digester during a relief event. • Improving reliability of level detection in the flash tanks as a lead indicator of a blocked flash tank outlet, <ul style="list-style-type: none"> ▪ Adding an additional level indicator to the three highest risk flash tanks, ▪ Based on feedback from level and other online indication (pressure) the valves will be closed by the control room. ▪ Long lead procurement for the entrainment separators and unit 2 relief tank have been approved. - Install second new oxalate tank. <ul style="list-style-type: none"> • This project was reassessed in light of a decarbonisation project to replace steam with electric vacuum pumps. • However due to the unknown schedule for the decarbonization projects it was decided to continue with the standby vent tank installation. • The first new vent tank can remain in duty until the standby is completed - Bottom fill precipitators – reduce turbulence in the top of the tanks during filling to stop alkali misting. <ul style="list-style-type: none"> • The emergent work, which includes the removal of redundant pipework has been fully scoped and is scheduled to be completed by quarter 2 2022, hence the schedule for completion of this project has been moved to 2023. - <p>Projects completed</p> <ul style="list-style-type: none"> - Existing equipment (identified as Class III and IV Risk) including piping, valving and fixtures on the Digester Pilot Steam Lines and the Flash Tank pilot steam lines have been replaced. - New oxalate vent tank has been installed and commissioned. - Upgrade and install shrouds on expansion joints;
----------------------	---

	<ul style="list-style-type: none"> - Flash tank relief header shroud installation; - Digestion heater vent diversion; - Flash tank relief header shroud installation; - Upgrade and install shrouds on expansion joints, - Remote stop for precip cooling towers – precip cooling tower fans to be stopped by the control room if conductivity of cooling water increases (conductivity increases are likely due to caustic liquor ingress) - HP blowdown line redirection – redirect blowdown lines to reduce steam and alkali at the entrainment separators. - Install an upgraded temperature control valve on the holding tanks contact heater steam supply line to manage steam supply to the contact heater, including stopping steam flow during upset conditions that may cause alkali emissions.
Comments	•

Implementation Schedule

Task	Alkali Release Off-Site																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Stage 2 Alkali Emissions Study	Complete																			
Bottom Fill Precipitators project	Study	Engineering	Execution	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Upgrade and install shrouds on expansion joints	Complete																			
Install 2nd oxalate tank				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
TCV and Steam shut off valve on holding tanks heater				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
HP blowdown line redirection				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Remote stop for precip cooling tower fans				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Digestion relief system containment system				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Digestion relief system front end				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete


Study Engineering Execution



 QUEENSLAND ALUMINA LIMITED

Alkali Release Off-Site


Legend

 Alkali and Odour Emissions Reduction

QUEENSLAND ALUMINA LIMITED
 This document is the property of Queensland Alumina Limited. It is to be used only for the purposes for which it was prepared and is not to be distributed, copied, or otherwise used without the prior written consent of Queensland Alumina Limited. Queensland Alumina Limited is not responsible for any loss or damage arising from the use of this document.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:8,119



N 	Review By:	J. JONATHAN
	Created By:	JONATHAN DALLON
	Approved By:	JONATHAN DALLON
	Approval No:	

Project (A2)	Alumina Dust Emission Reduction
Risk class	- III/High
Environmental risks	- Alumina dust emissions from Boyne Smelters Limited (BSL) conveyor transfer points, product load-out and island and mainland alumina storage A-frames have a potential to impact on the air quality of surrounding communities.
Project solution / options	- Identify options to reduce alumina dust emissions from high risk release points.
Objective / performance outcome	- Mitigation of alumina dust emissions
Performance Indicator	- No visible dust emissions from release points from completed projects.
Cost estimate A\$ million	- 23.0
Project Stage	<p>Engineering</p> <ul style="list-style-type: none"> - Projects focusing on the Island and Mainland A-frames have been moved into engineering and detailed design will focus on: <ul style="list-style-type: none"> • Automation of the reclaim system, • Improvements in the air slides in each A frame, and • New and upgraded dust collection systems, <p>Execution</p> <ul style="list-style-type: none"> - Alumina loadout, <ul style="list-style-type: none"> • Engineering design of a new ship loader and improvements to the wharf gallery and transfer tower is progressing towards 70%. <p>Complete</p> <ul style="list-style-type: none"> - BSL belt conveyor upgrade works
Comments	-

Implementation Schedule






Alumina Dust Emissions Reduction																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Alumina Loadout			Complete						Complete											
A-frames, alumina and hydrate transfer systems					Complete															
BSL alumina transfer upgrade	Complete																			
Island Shed Alumina Handling Upgrade																				
Mainland Shed Alumina Handling Upgrade																				
	Study	Engineering	Execution																	



 QUEENSLAND ALUMINA LIMITED

Alumina Dust Emissions


Legend

-  Ship Loadout
-  Island A Frame
-  BSL Conveyor and Transfer Points
-  Conveyors and Transfer Points
-  Mainland A Frame

© 2014 Queensland Alumina Limited. All rights reserved. This document is the property of Queensland Alumina Limited and is not to be distributed, copied, or otherwise used without the prior written consent of Queensland Alumina Limited.

Coordinate System: GDA 1984 MGA Zone 58

Scale at A3 1:12,834




N ↑	Revision	A
	Date	21/03/2018
	Created By	Jonathan Dalton
	Approved By	Jonathan Dalton

Project (A3)	Odour Emission to Community
Risk class	- III/High
Environmental risks	- Odour releases with potential for impact on air quality of surrounding communities.
Project solution / options	<ul style="list-style-type: none"> - Conduct an odour study including comparative analysis with previous 2006 study to determine an odour baseline - Capture current uncaptured organic emission sources, and - Address redundancy concerns with current treatment system
Objective / performance outcome	- Minimise QAL odour profile within the community
Performance Indicator	<ul style="list-style-type: none"> - Odour baseline is established when refinery is operating on Amrun bauxite. - Study phase identifies options to reduce emissions from odour sources in the refinery and they are progressed to engineering. - Selected engineering option is progressed to execution
Cost estimate A\$ million	- 39.5

Project Stage	<p>Air stripping is not being progressed, as barometric condensing is more effective</p> <ul style="list-style-type: none"> Air stripping of organics recycled in condensate from digestion. <ul style="list-style-type: none"> A pilot air stripping plant was installed on site and trialed stripping organics from the condensate stream. The outcomes of the trial showed that the air stripping did not target some of the highly odourous organics. In light of this QAL has identified a number of smaller projects targeting odourous streams for treatment utilising the barometric condensers. <p>Execution</p> <ul style="list-style-type: none"> Condensate reflash – Barometric condensing <ul style="list-style-type: none"> The first seawater condenser has been installed on Unit 2. The other condensers are being fabricated off-site. <p>Completed</p> <ul style="list-style-type: none"> Baseline odour sampling, Non-thermal plasma trial, Odour modelling based on baseline sampling, Wash water heater trial, <ul style="list-style-type: none"> The wash water heater trial demonstrated that odourous vapour can be condensed into the seawater flow sent to the waste tanks. The new thermal oxidizer (TO) has been commissioned and its operation will reduce down time where spent liquor heaters are venting directly to atmosphere. Evaporation heater vent condensate collection improvement project. <p>NTP Unit installation on Wash water tanks.</p>
Comments	<ul style="list-style-type: none">

Implementation schedule

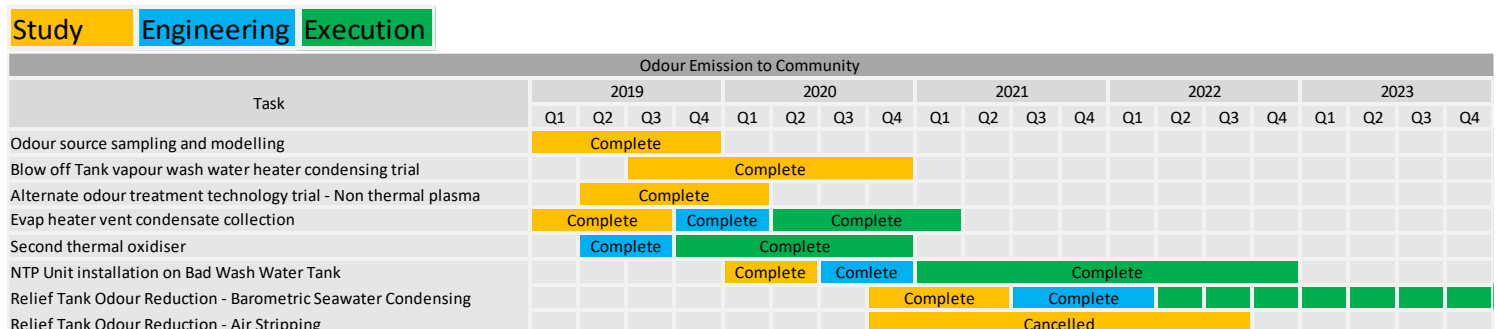





 **QUEENSLAND ALUMINA LIMITED**

Odour Emissions to Community


Legend

-  Alkali and Odour Emissions Reduction
-  Thermal Oxidiser

© 2014 Queensland Alumina Limited. All rights reserved. This document is the property of Queensland Alumina Limited and is not to be distributed, copied, or otherwise used without the prior written consent of Queensland Alumina Limited. Queensland Alumina Limited is not responsible for any errors or omissions in this document.

Coordinate System: GDA 1984 MGA Zone 58

Scale at A3: 1:5,553



N ↑	Revision	A
	Date	21/03/2018
	Created By	Jonathan Dalton
	Approved By	Jonathan Dalton

Project (A4)	Coal Stockpile Dust Emissions
Risk class	- III/High
Environmental risks	- Fugitive dust emissions from working and strategic coal stockpiles have the potential to impact on the air quality of surrounding communities.
Project solution / options	- Investigate options for dust mitigation, including dust suppression and prevention measures on working and strategic coal stockpiles.
Objective / performance outcome	- Improved monitoring capability and reduction of potential for dust emissions
Performance Indicator	- Reduced dust emissions from the coal stockpile.
Cost estimate A\$ million	- 1.0
Project Stage	Execution <ul style="list-style-type: none"> - Install upgraded sprinkler system on the working coal stockpile and dry fogging on the loadout hopper. <ul style="list-style-type: none"> • The project has been delayed due to cost escalations and supply issues arising from the pandemic and changes to legislation requiring additional electrical works.
Comments	<ul style="list-style-type: none"> - The strategic coal stockpile has been treated with a chemical sealant. - Upgraded water sprays have been chosen for dust mitigation at the working coal stockpile and dry fogging on the loadout hopper.

Implementation Schedule

Coal Stockpile Dust Mitigation																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Install upgraded spinkler system	Complete				Complete															

Study
Engineering
Execution

Project (A5)	Bauxite Transfer Dust Emissions
Risk class	- III/High
Environmental risks	- Fugitive dust emissions from bauxite transfer system have the potential to impact on air quality in the surrounding community.
Project solution / options	- Investigate options for reduction of dust emissions from the bauxite transfer system.
Objective / performance outcome	- Reduced dust emissions from bauxite transfer systems
Performance Indicator	- Bauxite dust emissions from return side of the wharf conveyor are mitigated.
Cost estimate A\$ million	- 0.8
Project Stage	Complete - Install a belt washer station and improved scrapers
Comments	- Results from a measuring system installed on the bauxite conveyor has identified carry back as a significant dust source.

Implementation Schedule


Bauxite Transfer Dust Reduction Study												
Task	2019				2020				2021			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Install belt wash station and upgrade scrapers	Complete	Complete	Complete	Complete								
Study	Engineering	Execution										



 QUEENSLAND ALUMINA LIMITED

Bauxite Transfer Dust Emissions


Legend

 Bauxite conveyor and transfer points

QUEENSLAND ALUMINA LIMITED (QAL) is a subsidiary of Rio Tinto Limited (RTO) and is a member of the Rio Tinto Group. This document is the property of QAL and is not to be distributed outside the organization. All rights reserved. QAL is not responsible for the accuracy or completeness of the information contained herein. QAL is not liable for any loss or damage arising from the use of this document.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:12,500



N 	Revision:	1
	Date:	20/03/2022
	Created By:	Jonathan DeLore
	Approved By:	Jonathan DeLore

Project (A6)	Ash Dam Dust Emissions
Risk class	- III/High
Environmental risks	- Fugitive dust (ash) emission emissions have the potential to impact on air quality of surrounding communities.
Project solution / options	- Investigate options for reduction of dusting events from the ash through dust suppression and mitigation options
Objective / performance outcome	- Minimise dust generation from #4 Ash Dam
Performance Indicator	- Ash dam dust is reduced after rain events.
Cost estimate A\$ million	- 4.5
Project Stage	Execution <ul style="list-style-type: none"> - Install new ring main and saltwater pump to provide seawater to be applied to Cell’s 3 and 4 during a rain event. <ul style="list-style-type: none"> • Work will begin in 2022 as there are external approvals requirements for this project. - Boilerhouse ash slurry pumps will be utilized to apply saltwater and ash to Cell 2 in the event of a rain event.
Comments	Dust occurs after rainfall, due to the fresh water breaking the salt crust formed on the surface of the cells.

Implementation Schedule

Study Engineering Execution


Ash Dam Dust Emissions																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Engineering for dust mitigation on ash dam	Complete				Complete															



 QUEENSLAND ALUMINA LIMITED

Ash Dam Dust Emissions


Legend

 Ash ponds

QUEENSLAND ALUMINA LIMITED
This map is a summary of the information contained in the Environmental Management System (EMS) and is not intended to be used as a substitute for the EMS. It is the responsibility of the user to ensure that the information is up to date and accurate. The information is provided as a guide only and should not be used for any other purpose. The information is provided as a guide only and should not be used for any other purpose.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:16,763



N 	Review By:	J. J. J.
	Created By:	J. J. J.
	Checked By:	J. J. J.
	Approved By:	J. J. J.

Water Management Improvement Projects

QAL's plan to improve water quality management over the next five years is supported by targets, actions and a program of works summarised below. Capital spend is estimated at between A\$90 million to A\$175 million.

Project (W1)	Raw Material Spill from Wharf
Risk class	- IV/Critical
Environmental risks	- Release of raw materials including caustic and bauxite to Gladstone harbour during unloading operations has the potential to impact on the water quality of Port Curtis.
Project solution / options	- Investigate options for reduction of spillage of raw materials (bauxite) from the wharf during unloading activities and mitigate the potential for release of caustic during unloading
Objective / performance outcome	- Reduce risk of release of raw material spills during unloading operations
Performance Indicator	- Gaps in the wharf are filled in.
Cost estimate A\$ million	- 0.75
Project Stage	Execution - Gaps within the wharf bunds provide pathways for materials to be released into the water.
Comments	

Implementation Schedule

Raw Material Spill from Wharf																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Fill in opennigs on wharf			■	■	■	■	■	■	■	■	■	■	■	■	■	■	■			
Study	■																			
Engineering		■	■	■	■	■	■	■	■	■	■	■	■	■	■	■	■			
Execution																				



 QUEENSLAND ALUMINA LIMITED

Raw Material Spill from Wharf


Legend

 Wharf - Raw Material Spill

QUEENSLAND ALUMINA LIMITED
This document is the property of Queensland Alumina Limited. It is to be used for the purposes stated in the title and for no other purpose. It is to be returned to Queensland Alumina Limited upon completion of the project. It is not to be distributed, copied, or otherwise used without the written consent of Queensland Alumina Limited.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3: 1:4,442



	Revision:	1
	Date:	28/03/2022
	Created By:	Jonathan DeLor
	Approved By:	Jonathan DeLor

Project W2	Coal Stockpile Stormwater Runoff
Risk class	- III/High
Environmental risks	- Release of coal contaminated stormwater to receiving environment has the potential to impact on the water quality in Port Cutis.
Project solution / options	- Investigate options for reduction in total suspended solids load from the coal stockpiles into the east and west coal stilling ponds, which allows ponds to meet release limits - Investigate options to improve west coal stilling pond neutralisation capability
Objective / performance outcome	- Mitigate risk of coal contaminated stormwater leaving the coal stockpile catchment area
Performance Indicator	- Study phase identifies options to reduce coal fines runoff from coal stockpiles in the refinery and improve neutralisation capacity of the west coal stilling pond and they are progressed to engineering.
Cost estimate A\$ million	- 2.2
Project Stage	<p>Engineering</p> <p>Phase 2:</p> <ul style="list-style-type: none"> - Improvement in neutralisation capability in the west coal stilling pond, including <ul style="list-style-type: none"> • Automation of the seawater inlet valve, • Improved seawater distribution to maximise mixing. <p>Complete</p> <ul style="list-style-type: none"> - TSS functionality improvements for the west coal stilling pond have been completed, including: <ul style="list-style-type: none"> • Works to stop seepage around the weir, • Re-establish the functionality of the dividing wall for sediment control and contaminated water segregation. <ul style="list-style-type: none"> ▪ Install additional fingers to lengthen the flow path and allow for easier desilting. - Phase 2- Extension of the west coal stilling pond to provide additional storage and neutralization capability.
Comments	

Implementation Schedule

Coal Stockpile Stormwater Runoff																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Phase 2 Study	Complete																			
Improve west coal stilling pond functionality - Neutralisation									Complete											
Improve west coal stilling pond functionality - TSS					Complete				Complete											

Study
Engineering
Execution




Coal Stockpile Runoff

Legend

- East Coal Stilling Pond
- West Coal Stilling Pond
- Strategic Coal Stockpile
- Working Coal Stockpile

DATE: 08/03/2022
 DRAWN BY: J. DALLON
 CHECKED BY: J. DALLON
 APPROVED BY: J. DALLON

Scale at A3 1:9,884



N
 Review: J. DALLON
 Date: 08/03/2022
 Checked By: J. DALLON
 Approved By: J. DALLON

Project (W3)	Waste line 4 Integrity
Risk class	- IV/Critical
Environmental risks	- Failure of Waste Line 4 into marine or terrestrial environments will result in release of partially neutralised red mud with a potential to contaminate land or water and impact on the water quality in South Trees Inlet and Port Curtis.
Project solution / options	- Investigate options for replacement of waste line 4 capacity that includes options that further reduces the risk of a pipeline failure. - Ensure integrity of pipeline supports
Objective / performance outcome	- No loss of containment incidents
Performance Indicator	- 20 years life of waste line 4 with minimal risk of loss of containment incidents
Cost estimate A\$ million	- 50.95
Project Stage	Complete
Comments	- A leak detection system will be installed in Q1 2022..

Implementation Schedule

Waste Line 4 Capacity																		
Task	2018		2019				2020				2021				2022			
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
Waste line 4 capacity replacement	Complete		Complete				Complete				Complete							
Study																		
Engineering																		
Execution																		



 QUEENSLAND ALUMINA LIMITED

Waste Line 4


Legend

 Waste Line 4

QUEENSLAND ALUMINA LIMITED
This map is a site plan for the Waste Line 4 project. It shows the location of the waste line and the surrounding area. The map is for informational purposes only and should not be used for any other purpose. All rights reserved.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3: 1:44,421



	Revised By:	J. JONATHAN DALLIN
	Created By:	JONATHAN DALLIN
	Checked By:	JONATHAN DALLIN
	Approved By:	JONATHAN DALLIN

Project (W4)	East & West Contaminants Ponds
Risk class	- III/High
Environmental risks	- The East and West contaminants ponds capture contaminated stormwater runoff for recycling into the process. Insufficient capacity has the potential to impact the capability of the contaminated stormwater treatment system prior to release and has a potential to impact on the water quality in Port Curtis. A further potential impact exists for groundwater from the unlined east contaminants pond.
Project solution / options	- Investigate options to ensure that all core refinery process areas are directed to a contaminants pond, - Options for lining and expanding the east contaminants pond, and - Investigate options to increase the pump and pipe capacity from the ponds to the process.
Objective / performance outcome	- Ensure containment ponds prevent land and groundwater contamination and mitigates the risk of stormwater contamination
Performance Indicator	- Study phase identifies options to prevent land and groundwater contamination from contaminants ponds and they are progressed to engineering.
Cost estimate A\$ million	- 11.2
Project Stage	<p>Engineering</p> <ul style="list-style-type: none"> - Detailed design of the east contaminates pond (ECP) will look at: <ul style="list-style-type: none"> • Lining of the existing ECP, • Installation of a new tanks adjacent to the waste transfer facility. <p>Execution</p> <ul style="list-style-type: none"> - Install new pump in west contaminates pond and pipeline to east contaminates pond.
Comments	<p>The contaminates pond project has been spilt into two specific focus projects;</p> <ul style="list-style-type: none"> • West contaminates pond pump upgrade and piping. • East contaminates pond location and lining options. • This has been done in respect of the different levels of effort that need to be applied to each of the ponds.

Implementation Schedule

East and West Contaminants Ponds																				
Task	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
West contaminates pond				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
East contaminates pond				Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Study	Engineering	Execution																		



Contaminants Ponds


Legend

- East Pond
- West Pond

Disclaimer: © 2016 QAL (ASX: QAL) and RUSAL (NYSE: RUSAL) make no representation or warranty as to the accuracy, completeness or reliability of any information provided. QAL and RUSAL do not warrant or accept any liability for any loss or damage, including consequential, special or exemplary damages, arising from the use of this information. This information is provided for general information only and should not be relied upon for any specific purpose.

Coordinate System: GDA 1994 MGA Zone 58

Scale at A3: 1:4,274



N 	Revision	A
	Date	21/03/2022
	Created By	Jonathan Dalton
	Reviewed By	Jonathan Dalton

Project (W5)	Refinery Water Release Management
Risk class	- III/High
Environmental risks	- Releases from the sweetening bauxite pond and the west gate wetland have the potential to impact on water quality in Port Cutis.
Project solution / options	- Investigate options to improve monitoring at the sweetening bauxite pond and the wetland release - Identify options to upgrade mill sump water system to minimise release to the stormwater system
Objective / performance outcome	- Ensure pH, suspended solids and other release water quality parameters are maintained within limits and no uncontrolled release to receiving environment
Performance Indicator	- Study phase identifies options to improve water quality at the west gate wetland, mill 10 area and sweetening bauxite pond and they are progressed to engineering. - 85% availability of online instruments at the sweetening bauxite pond and wetland release point
Cost estimate A\$ million	- 5.2

Project Stage	<p>Execution – Phase 2</p> <ul style="list-style-type: none"> - Westgate pond - Improve capacity and functionality: <ul style="list-style-type: none"> • Increase capacity of the pond • Install mid pond continuous pH monitoring, • Relocate the seawater discharge location to allow for better access and mixing in the pond. - Mill 10 sump; <ul style="list-style-type: none"> • Improve management of bauxite in the bund, • Ensure grades within the bund are correct, • Install an additional drive-in sump to allow for collection of bauxite and fast reclaim. - Bauxite Sweetening Pond: <ul style="list-style-type: none"> • Pre-treatment pond to reduce bauxite and bauxite fines from the mono bauxite stockpile entering the bauxite sweetening pond. • Delays to the project were experienced due to unexpected historic landfill materials found during excavation of the pre-treatment pond. • It is expected that this project will be completed in Q2 2023. <p>Complete – Phase 1</p> <ul style="list-style-type: none"> - Wetland Release: <ul style="list-style-type: none"> • V-notch weir and flow meter installed, • Continuous water quality monitoring installed. - Sweetening Bauxite Pond <ul style="list-style-type: none"> • Continuous water quality monitoring installed, • A level sensor installed.
Comments	

Implementation Schedule





Study Engineering Execution

Task	Refinery water release improvement																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Phase 2 Study				Complete																
Install V notch weir and continuous monitoring at Westgate Release Point	Complete																			
Install continuous monitoring at sweetening bauxite pond Release Point	Complete																			
Mill 10 bauxite stormwater pre-treatment upgrade								Complete												
Westgate pond improvements								Complete												
Bauxite sweetening pond bauxite stormwater runoff Pretreatment from mono stockpile								Complete												




 QUEENSLAND ALUMINA LIMITED

**Refinery
Stormwater
Legend**

-  Mill 10 Area
-  Sweetener Pond
-  Bauxite Pond
-  West Gate Release

Details of this plan shall be subject to the conditions of the relevant licence and permit. This plan is for information only and does not constitute a contract. It is subject to change without notice. The user of this plan shall be deemed to have accepted the conditions of use and shall be responsible for ensuring that the plan is used in accordance with the relevant licence and permit.

Coordinate System: GDA 1984 UTM Zone 58
Scale at A3: 1:11,105



N 	Revision:	1
	Created By:	Jonathan Dallas
	Checked By:	Jonathan Dallas
	Approved By:	Jonathan Dallas

Project (W6)	RDA Surface/Ground water Impacts
Risk class	- IV/Critical
Environmental risks	- Impacts to surface and groundwater from the RDA that have the potential to impact on the water quality in South Trees Inlet and Port Curtis and terrestrial ecosystems surrounding the RDA.
Project solution / options	- Identify the sources, pathways and receptors of potential RDA surface and groundwater impacts and options for any required mitigation.
Objective / performance outcome	- Prevent impact of contaminants from RDA on groundwater - Mitigate the impact of the RDA on adjacent surface water systems and ensure relevant environmental values are protected
Performance Indicator	- Vegetation in the Black Breasted Button Quail (BBBQ) habitat does not show any signs of degradation and rehabilitated areas (to be completed) show no sign of impact after cut off wall is installed and soil in impacted areas is flushed. - A robust monitoring program is in place for the early detection of impact to vegetation, groundwater and marine communities. - Study phase (Environmental Evaluation) identifies options to address any areas of concern and these options are progressed to engineering. - Engineering options are progressed to execution
Cost estimate A\$ million	- 54

<p>Project Stage</p>	<p>Engineering</p> <ul style="list-style-type: none"> - HRMD (historic red mud dam) north and west seepage mitigation. Designs for cut off walls and drains have reached 60%, however further engineering is required to investigate options to modernise the original HRMD embankment and to also provide a seepage mitigation option. - RMD 1 GW seepage <ul style="list-style-type: none"> • Groundwater modelling and monitoring identified a section along the eastern wall of red mud dam 1 where seepage was being released. • A cut off wall and surface drain are being engineered to mitigate this exposure area. <p>Execution</p> <ul style="list-style-type: none"> - RMD 2 NE Corner SW <ul style="list-style-type: none"> • This project will manage seepage from the north east corner of red mud dam 2 and return it to the red mud dams <p>Completed</p> <ul style="list-style-type: none"> - EE Stage 1 – install cut-off wall to mitigate impact on BBBQ bird habitat; - EE Stage 2 – Install a cut off wall along the eastern side of the HRMD. - Install a drain along the eastern side of the HRMD. - Install a cut off wall and drain along the western side of the northern decant pond – cell 1 to intercept potential seepage from the pond.
<p>Comments</p>	<ul style="list-style-type: none"> - Groundwater removal on the dam side of the cut-off wall at the BBBQ habitat has resulted in sustained lower water levels demonstrating that the cut-off wall is functioning as designed. <ul style="list-style-type: none"> • BBBQ movements have been recorded in the habitat; <ul style="list-style-type: none"> ▪ A survey identified 95 BBBQ movements in 2021 compared to 0 in 2016. -

Implementation Schedule

Task	RDA Surface/Groundwater Impacts																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
EE Stage 1 - Install cut-off wall to mitigate impact on BBBQ habitat and recovery pumps	Complete																			
EE Stage 2 - Install cut-off wall/trench along eastern side of historical RDA		Complete			Complete															
Cell 1 cut-off wall and drain									Complete											
HRMD North and West Seepage Mitigation																				
RMD 2 NE Corner SW															Complete					
RMD 1 GW seepage																				

Study
Engineering
Execution



RDA Groundwater Impacts

Legend

- EE Stage 1
- EE Stage 2

Disclaimer: © 2016 QAL, (ASX: QAL) and RUSAL, (NYSE: RUSAL) are the joint owners of the RDA. This map is for informational purposes only and does not constitute an offer of any financial product. It is not intended to be used as a basis for investment decisions. The map is not to be used as a basis for investment decisions. The map is not to be used as a basis for investment decisions.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:39,597

0 220.440 880 1,320

Meters

N
Revision A
Date 21/02/2022
Created By Jonathan Dalton
Reviewed By
Approved By Jonathan Dalton

Project (W7)	RDA Release to Receiving Environment
Risk class	- IV/Critical
Environmental risks	- The chemistry of the red mud dam discharge into South trees Inlet has been changing over the past 5 to 10 years. This, together with the siltation of South Trees Inlet and decrease in water flow, has resulted in low dissolved oxygen between the discharge site and confluence of the Boyne River and has the potential to impact on the water quality in South Trees Inlet and the Boyne River.
Project solution / options	- Identify the cause of the change in water quality and investigate mitigation options, including improvements to release water quality, alternative release point locations or improving flow in South Trees Inlet.
Objective / performance outcome	- Ensure the environmental values of South Trees Inlet are protected in the long term
Performance Indicators	- Study phase identifies options to reduce the impact of the RDA discharge and options are progressed to engineering. - Engineering options are progressed to execution. - Cell 1 operation reduces BOD
Cost estimate A\$ million	- 70.0
Project Stage	<p>Engineering</p> <ul style="list-style-type: none"> - Alternate Discharge Location <ul style="list-style-type: none"> • Modelling of the three possible alternate release points has shown that the QAL wharf is the most suitable location and will be progressed into engineering. <p>Execution</p> <ul style="list-style-type: none"> - Cell 2 of the northern management and treatment area has entered the construction phase and will be linked with cell 1 when completed. <ul style="list-style-type: none"> • Operation of cell 1 will provide information that will assist with determining the ultimate size of cell 2. <p>Complete</p> <ul style="list-style-type: none"> - Construction of Cell 1 of the northern decant management and treatment area has been completed.

Comments	<ul style="list-style-type: none"> - Two facultative treatment cells have been chosen to treat the seawater before it is returned South Trees Inlet. - The BSL or QAL wharf have been chosen as an alternate release point.
----------	---

Implementation Schedule

Task	RDA Alternative Discharge Location																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Northern Decant Pond - Cell 1				Complete	Complete	Complete	Complete	Complete												
Northern Decant Pond - final configuration									Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete
Alternate Discharge Location									Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete	Complete

Study **Engineering** **Execution**



RDA Discharge

Legend

-  Licenced Discharge Point

Queensland Alumina Limited (QAL) is a subsidiary of Rio Tinto Limited (RTO). This map is for informational purposes only and does not constitute a contract or offer of any financial product. It is subject to change without notice. For more information, please contact the relevant department.

Coordinate System: GDA 1984 UTM Zone 56

Scale at A3 1:44,421

0 245 490 980 1,470

Meters



Review:	J. Williams
Created by:	Jonathan Dallas
Approved by:	Jonathan Dallas

Project (W8)	High Risk Pipelines
Risk class	- IV/Critical
Environmental risks	- Caustic release to the environment as a result of failure of pipeline from the storage area (island) to refinery (mainland) across causeway with potential to impact on the water quality in Port Curtis.
Project solution / options	- Investigate options to upgrade high risk pipelines (caustic and contaminated water) to reduce the risk of a pipeline failure
Objective / performance outcome	- Reduce the risk of off-site contamination
Performance Indicator	- High risk pipelines are installed to provide a 20 year life with a reduction in likelihood of failure.
Cost estimate A\$ million	- 10.5
Project Stage	Complete
Comments	

Implementation Schedule


High Risk Pipelines																
Task	2019				2020				2021				2022			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Investigate options for replacement of high risk pipelin	Comple	Complete			Complete											
	Study	Engineering	Execution													



 QUEENSLAND ALUMINA LIMITED


High Risk Pipelines

Legend

 High Risk Pipelines

QUEENSLAND ALUMINA LIMITED
This map is a summary of the information contained in the GIS database and is not intended to be used as a substitute for the GIS database. It is not intended to be used for legal purposes. The information contained in this map is for informational purposes only. The information contained in this map is not intended to be used for legal purposes. The information contained in this map is for informational purposes only.

Coordinate System: GDA 1984 UTM Zone 58
Scale at A3: 1:11,096



N 	Revision:	1
	Date:	20/03/2022
	Created By:	Jonathan DeLore
	Approved By:	Jonathan DeLore

Land management improvement projects

QAL's five-year land stewardship programme, supported by targets, actions and a programme of works is summarised below. Capital spend is estimated at between A\$20 million to A\$35 million.


Project (L1)	Integrity of Bunds and Drains
Risk class	- IV/Critical
Environmental risks	- Seepage from bunded refinery areas has the potential to contaminate groundwater.
Project solution / options	- Bunded refinery area and drainage integrity rectification.
Objective / performance outcome	- Restore the integrity of refinery area bunds and drains
Performance Indicator	- All areas identified for remediation are repaired
Cost estimate A\$ million	- 39.3
Project Stage	<p>Execution</p> <ul style="list-style-type: none"> - Bunds in execution: <ul style="list-style-type: none"> • HID1/5 bund repair, and • Filter Press South Floor • HID 2/6 bund, • Fill tanks 1&2 bund, • Secondary settler No. 7 sump, • Tertiary Tanks 7,8,9 sump, and • F/G row sump and bund. - Drains in execution <ul style="list-style-type: none"> • East West Road (Above Ground) drain, • Papa Street drain, • East West Road (Below Ground) drain, • Lima Street drain. <p>Completed</p> <ul style="list-style-type: none"> • Above ground section of 7th street drain, • HID ¾, • A precipitation row concrete remediation works, • Tertiary tanks 1-4 nib wall replacement, and • Sulphuric acid tank bund interim remediation. • 5th Street drain, • EF row concrete remediation works, and • Bravo Street Drain. • Sierra Street Drain. • Tertiary tank 5 bund repairs, and • 9th Street Drain • New sulphuric acid storage and handling facility • 1st Street Drain (above ground), and • November Street Drain (above ground)

Comments	- The Bund and drain inspection program has identified high, medium and low risk bunds and drains requiring remediation.
----------	--

Implementation Schedule

Task	Integrity of bunds and Drains																								
	2018				2019				2020				2021				2022				2023				
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
5th Street Drain repairs				Complete																					
Bravo Street Drain repair				Complete																					
Sierra Street Drain repairs				Complete																					
Installation of new sulphuric acid storage facility							Complete																		
EF Row concrete remediation works						Complete																			
Tertiary tanks 1-4 nib wall replacement				Complete																					
Sulphuric acid tank interim bund remediation				Complete																					
Above Ground Section of Seventh Street Drain repair	Complete																								
HID 3/4 bund repair	Complete																								
HID 1/5 bund repair																									
Tertiary tank 5 bund remediation							Complete																		
9th Street drain repairs							Complete																		
1st Street Drain (above ground)													Complete												
November Street Drain (above ground)													Complete												
Filter Press South Floor																									
East West Road (Above Ground) drain																									
Papa Street Drain																									
East West Road (Below Ground) drain																									
Lima Street drain																									
HID 2/6 Bund																									
Fill Tanks 1&2 Bund																									
Secondary Settler 7 sump																									
Tertiary Tanks 7,8,9 sump																									
F/G Row sump and bund																									

Study Engineering Execution

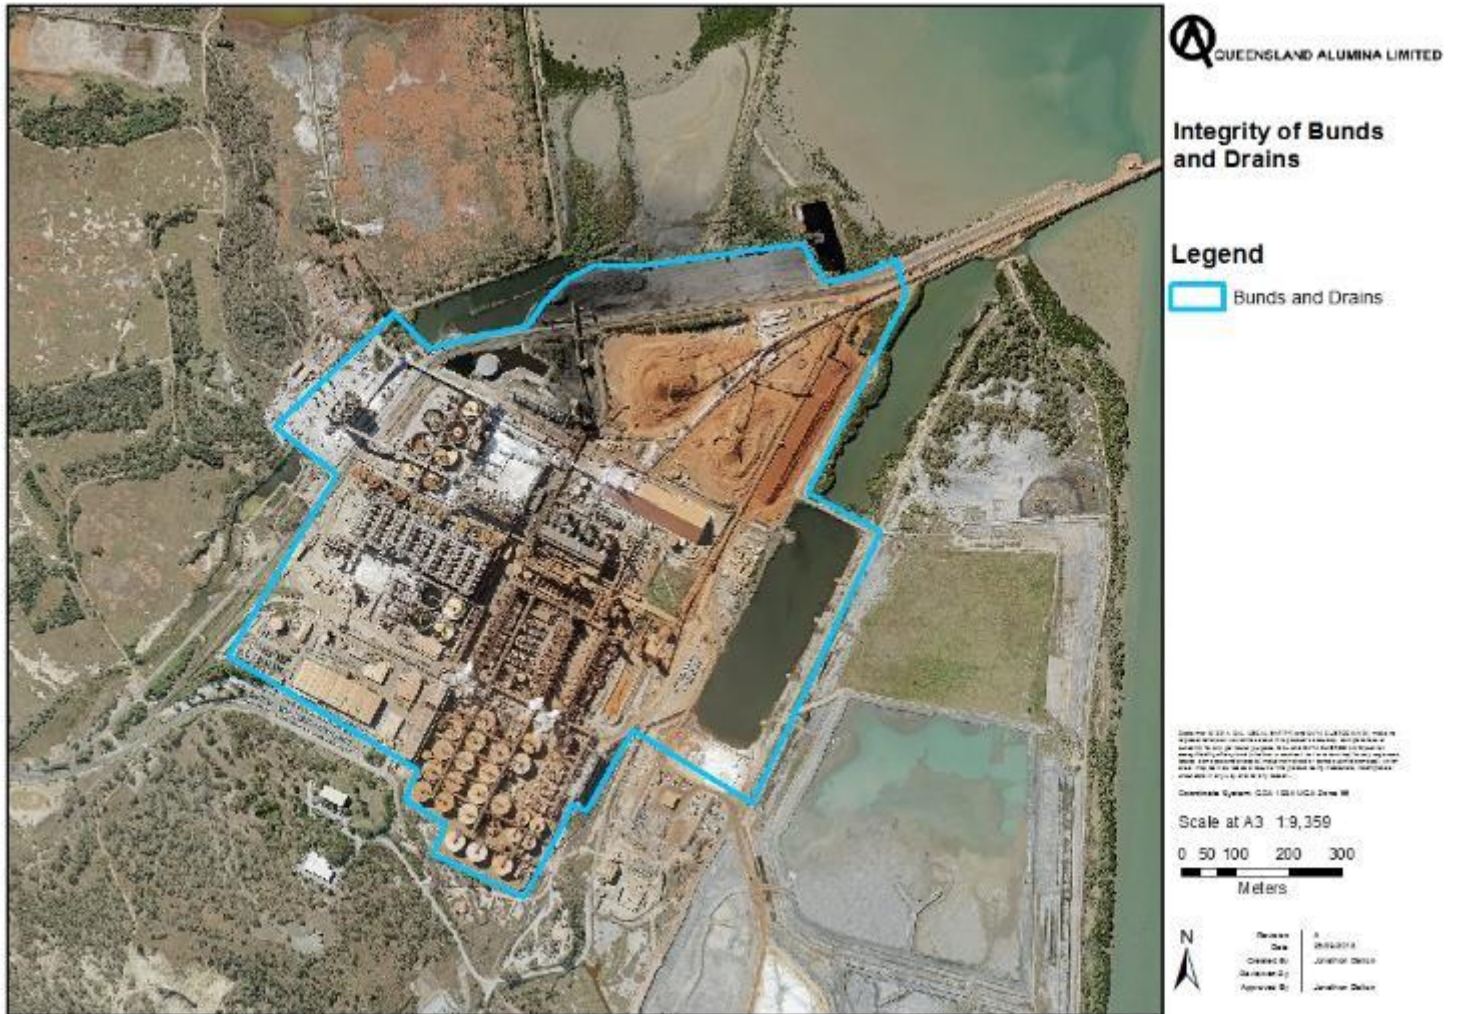

Project (L2)	Ground Water Impact to South Trees Island Tank Farm
Risk class	- III/High
Environmental risks	- Caustic impact to ground water and potential to migrate to receiving environment (DES EPO STAT 1249 related) and has the potential to impact on groundwater quality.
Project solution / options	- Maintain and monitor current extraction program beneath bund 4, South Trees Island - Review integrity of existing groundwater monitoring wells reinstate/upgrade as necessary and recommence monitoring program
Objective / performance outcome	- Historic ground water impact to South Trees Island does not migrate and is reduced over time
Performance Indicator	- No increase in pH in groundwater bores outside of bund with extraction system operational

Cost estimate A\$ million	- 1.0
Project Stage	Completed
Comments	<ul style="list-style-type: none"> - Groundwater pumping is ongoing. - Monitoring of groundwater will continue and opportunities to improve the system will continue to be investigated based on the results of the ongoing monitoring.



Groundwater Impacts at South Trees Island Tank Farm


Legend

- Bund 2
- Bund 4

Copyright © 2014, Rio Tinto Alcan. All rights reserved. This document is confidential and its disclosure is restricted to the intended recipients only. It is not to be distributed, copied, or otherwise used without the prior written consent of Rio Tinto Alcan. If you are not an intended recipient, please notify the sender immediately.

Coordinate System: GDA 1984 MGA Zone 58

Scale at A3 1:2,981



	Revision	A
	Date	21/03/2015
	Created By	Jonathan Dalton
	Reviewed By	Jonathan Dalton

Project (L3)	Mineral Waste Disposal Facility – Stage 2
Risk class	- III/High
Environmental risks	- Potential for land contamination from landfilled mineral wastes and potential for impact on water quality in South Trees Inlet; secondary potential impact to effectiveness of current recycling program
Project solution / options	- Investigate the options for location of another mineral waste disposal facility - Investigate options to ensure design improves land contamination controls
Objective / performance outcome	- Execute the design for the mineral waste disposal facility.
Performance Indicator	- Minimise and contain leachate from the mineral waste disposal facility.
Cost estimate A\$ million	- 2.6
Project Stage	<p>Execution</p> <ul style="list-style-type: none"> - Mineral Waste Disposal Facility stage 2 <ul style="list-style-type: none"> • Unsuitable ground conditions were identified at the start of construction, requiring further engineering design. • It is expected that the MWDF stage 2 will be completed by the end of Q3 2023. <p>Complete</p> <ul style="list-style-type: none"> - An interception drain located south of the mineral waste disposal facility has been identified as the best option to minimise the risk of seepage migration.
Comments	<ul style="list-style-type: none"> - Execution schedule has been significantly delayed and estimated completion is now expected in 2022, <ul style="list-style-type: none"> • Additional detailed design has been identified in additional scope items, including the western diversion drain and upgrades to the leachate sump pumping. • Seepage mitigation has been included as a separate co-committed project.

Implementation Schedule

Task	Mineral Waste Disposal Facility																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Implement design for stage 2 of the MWDF	Complete																			
Mineral waste seepage mitigation							Complete		Complete				Complete							
	Study	Engineering	Execution																	




QUEENSLAND ALUMINA LIMITED

Mineral Waste Facility - Stage 2

Legend

Mineral Waste Facility

Details of this plan, specification and drawings shall be taken from the latest revision of the project documents. Any amendments to the drawings shall be indicated by a revision number and date. The drawings shall be used in accordance with the project documents. The drawings shall be used in accordance with the project documents.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:9,359

0 50 100 200 300
Meters

N

Revised By:	J. Delaney
Checked By:	Jonathan Delaney
Approved By:	Jonathan Delaney

Project (L4)	Sewerage System Upgrade
Risk class	- III/High
Environmental risks	<ul style="list-style-type: none"> - Potential for land contamination from sewerage system installed during initial and subsequent plant construction phases and potential to contaminate groundwater. - Introduction of inadequately treated effluent to the RDA
Project solution / options	<ul style="list-style-type: none"> - Investigate the condition of the sewerage system to identify issues and assess options to rectify identified issues - Review the current operation of the sewage treatment system and look at requirement for upgrade
Objective / performance outcome	- Reduce the risk of the release of sewage to land
Performance Indicator	- Sewerage system is fully functional
Cost estimate A\$ million	- 2.0
Project Stage	Execution <ul style="list-style-type: none"> - Refurbish existing sewage treatment plant, and - Install a new pipeline to the treatment plant to replacing the section with the leak.
Comments	- A temporary repair to the sewage pipelines is in place.

Implementation Schedule


Task	Sewerage System																			
	2019				2020				2021				2022				2023			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Complete engineering for the sewerage system at the refinery	Complete				Complete															
	Study	Engineering	Execution																	



 QUEENSLAND ALUMINA LIMITED

Sewerage System Review


Legend

 Sewage Treatment Plant

QUEENSLAND ALUMINA LIMITED
This document is the property of Queensland Alumina Limited. It is to be used only for the purposes for which it is prepared and is not to be distributed, copied, or otherwise used without the prior written consent of Queensland Alumina Limited. Queensland Alumina Limited is not responsible for any loss or damage arising from the use of this document.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3: 1:4,600



	Reviewed By:	J. DELANEY
	Checked By:	JONATHAN DELANEY
	Drawn By:	JONATHAN DELANEY
	Approved By:	JONATHAN DELANEY

Project (L6)	Closure Pilot - RDA rehabilitation
Risk class	- II/medium
Environmental risks	- Implementation of a long term effective cover system for closure at the RDA
Project solution / options	- Undertake research of cover systems for closure of the RDA.
Objective / performance outcome	- Determine if a long term cover system can be sustained at the RDA.
Performance Indicator	- Study phase identifies options for long term remediation of the red mud dams. - Trial plot at RDA sustains vegetation to show proof of concept for the project.
Cost estimate A\$ million	- 1.75
Project Stage	Engineering - The remaining four years of the strategy will determine the long term viability of making technosoils from red mud.
Comments	- A Pilot rehabilitation trial is established at the Residue Disposal Area. - QAL and the University of Queensland were recognised with the 2019 Partners in Research Excellence Awards for work on the development of technosoils at the RDA.

Implementation Schedule

RDA Closure Rehabilitation																								
Task	2018				2019				2020				2021				2022				2023			
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4			
Investigate closure cover options for the RDA	Complete																							


Study Engineering Execution



 QUEENSLAND ALUMINA LIMITED

RDA Rehabilitation - Pilot Study


Legend

 Rehabilitation Trial Area

QUEENSLAND ALUMINA LIMITED
 This document is the property of Queensland Alumina Limited. It is to be used only for the purposes stated in the title and for the specific project mentioned. It is not to be distributed, copied, or otherwise used without the written consent of Queensland Alumina Limited.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:9,359



	Revised By:	J. DELANEY
	Created By:	JONATHAN DELANEY
	Checked By:	JONATHAN DELANEY
	Approved By:	JONATHAN DELANEY

Project (L7)	Oil/water facility resizing
Risk class	- II/Medium
Environmental risks	- Land contamination from oily wastes with the potential to impact groundwaters and the water quality in South Trees Inlet.
Project solution / options	- Install an oil/water separator at the waste transfer facility
Objective / performance outcome	- To improve management of oily wastes.
Performance Indicator	- Management of oily/water on site is improved. - Oil spills at the refinery are reduced.
Cost estimate A\$ million	- 0.835
Project Stage	Complete - All oil/water separator and storage facility has been completed and has been commissioned.
Comments	- This facility provides a permanent location for the storage of oil waste prior to transport off-site to a recycling facility.

Implementation Schedule

Oil/water Separation Facility										
Task	2018	2019				2020				
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
Complete design for upgrade to oil/water separator at waste transfer station	Complete	Complete								


Study Engineering Execution



 QUEENSLAND ALUMINA LIMITED

Proposed Oil Water Facility


Legend

 Oil water facility

QUEENSLAND ALUMINA LIMITED
 This document is the property of Queensland Alumina Limited. It is to be used only for the purposes for which it is prepared and is not to be distributed, copied, or otherwise used without the prior written consent of Queensland Alumina Limited. Queensland Alumina Limited is not responsible for any errors or omissions in this document. Queensland Alumina Limited is not liable for any loss or damage, including consequential loss or damage, arising from the use of this document.

Coordinate System: GDA 1984 UTM Zone 58

Scale at A3 1:7,019



North Arrow	Revision	1
	Date	20/03/2022
	Created By	Jonathan Deane
	Checked By	Jonathan Deane
	Approved By	Jonathan Deane

Project (L8)	Strategy for Caustic Storage
Risk class	- III/High
Environmental risks	- Current South Trees Island storage location has risks (substrate) for location of a tank farm and a risk of groundwater contamination.
Project solution / options	- Investigate options for a long term caustic storage tank farm.
Objective / performance outcome	- Confirm current locations suitability for the tank farm or; - Identify suitable alternate locations for the caustic storage tank farm
Performance Indicator	- Execution phase – all operational caustic storage tanks are inspected, all faults repaired and returned to service with RPEQ signoff.
Cost estimate A\$ million	- 18.1
Project Stage	Completed - Tank 1515 - Tank T15Q005 - Tank T15Q006
Comments	- QAL has decided to continue to store caustic soda in bunds 2 and 4 at South Trees Island. - All operational caustic storage tanks in bunds 2 and 4 at South Trees Island have been brought off-line, cleaned, inspected and any faults rectified prior to the tanks being returned to service. - Tank T15Q006 has been brought offline and an access hole has been cut into the side of the tank and the clean out process has commenced.

Implementation Schedule

Caustic Storage Strategy								
Task	2019				2020			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Inspect and repair tank T1515	Complete							
Inspect and repair tank T15Q005			Complete					
Inspect and repair tank T15Q006				Complete				

Study
Engineering
Execution

Other Environmental Improvement Projects

In addition to projects that address the specific environmental parameters of air, water and land, projects that address other aspects of the operation have also been identified below.

Project (O1)	Noise Emissions
Risk class	- III/High
Environmental risks	- Community noise impact from operational and maintenance works
Project solution / options	- Review current noise impact management including: <ul style="list-style-type: none"> • Efficacy of implemented controls on hydro-blasting • Adequacy of noise monitoring program; • Noise source assessment; • Plant and equipment noise mitigation options; and • Operational improvements (e.g. timing of noisy work practices)
Objective / performance outcome	- Reduce QAL noise footprint
Performance Indicator	- Study phase – <ul style="list-style-type: none"> • Verifies high risk noise sources are adequately managed.
Cost estimate A\$ million	- 0.4
Project Stage	Study <ul style="list-style-type: none"> • Complete Completed Projects <ul style="list-style-type: none"> • Emergency diesel generator building noise reduction paneling has been installed.
Comments	- Noise surveys show that QAL meets the EA conditions, - High noise generating activities, such as hydroblasting are regulated through on-site procedures that limit the time these activities can be undertaken. Specific high noise exposure areas will be targeted in conjunction with occupational hygiene projects. These projects will target plant and equipment that exceed occupational exposure limits and will have an improvement on environmental noise.

Implementation Schedule

Noise Emissions

Task	2018	2019				2020			
	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Review current noise impact management						Complete			

Study Engineering Execution
